




Project: CFWI MASTER 040116
Date: Thu 6/9/16



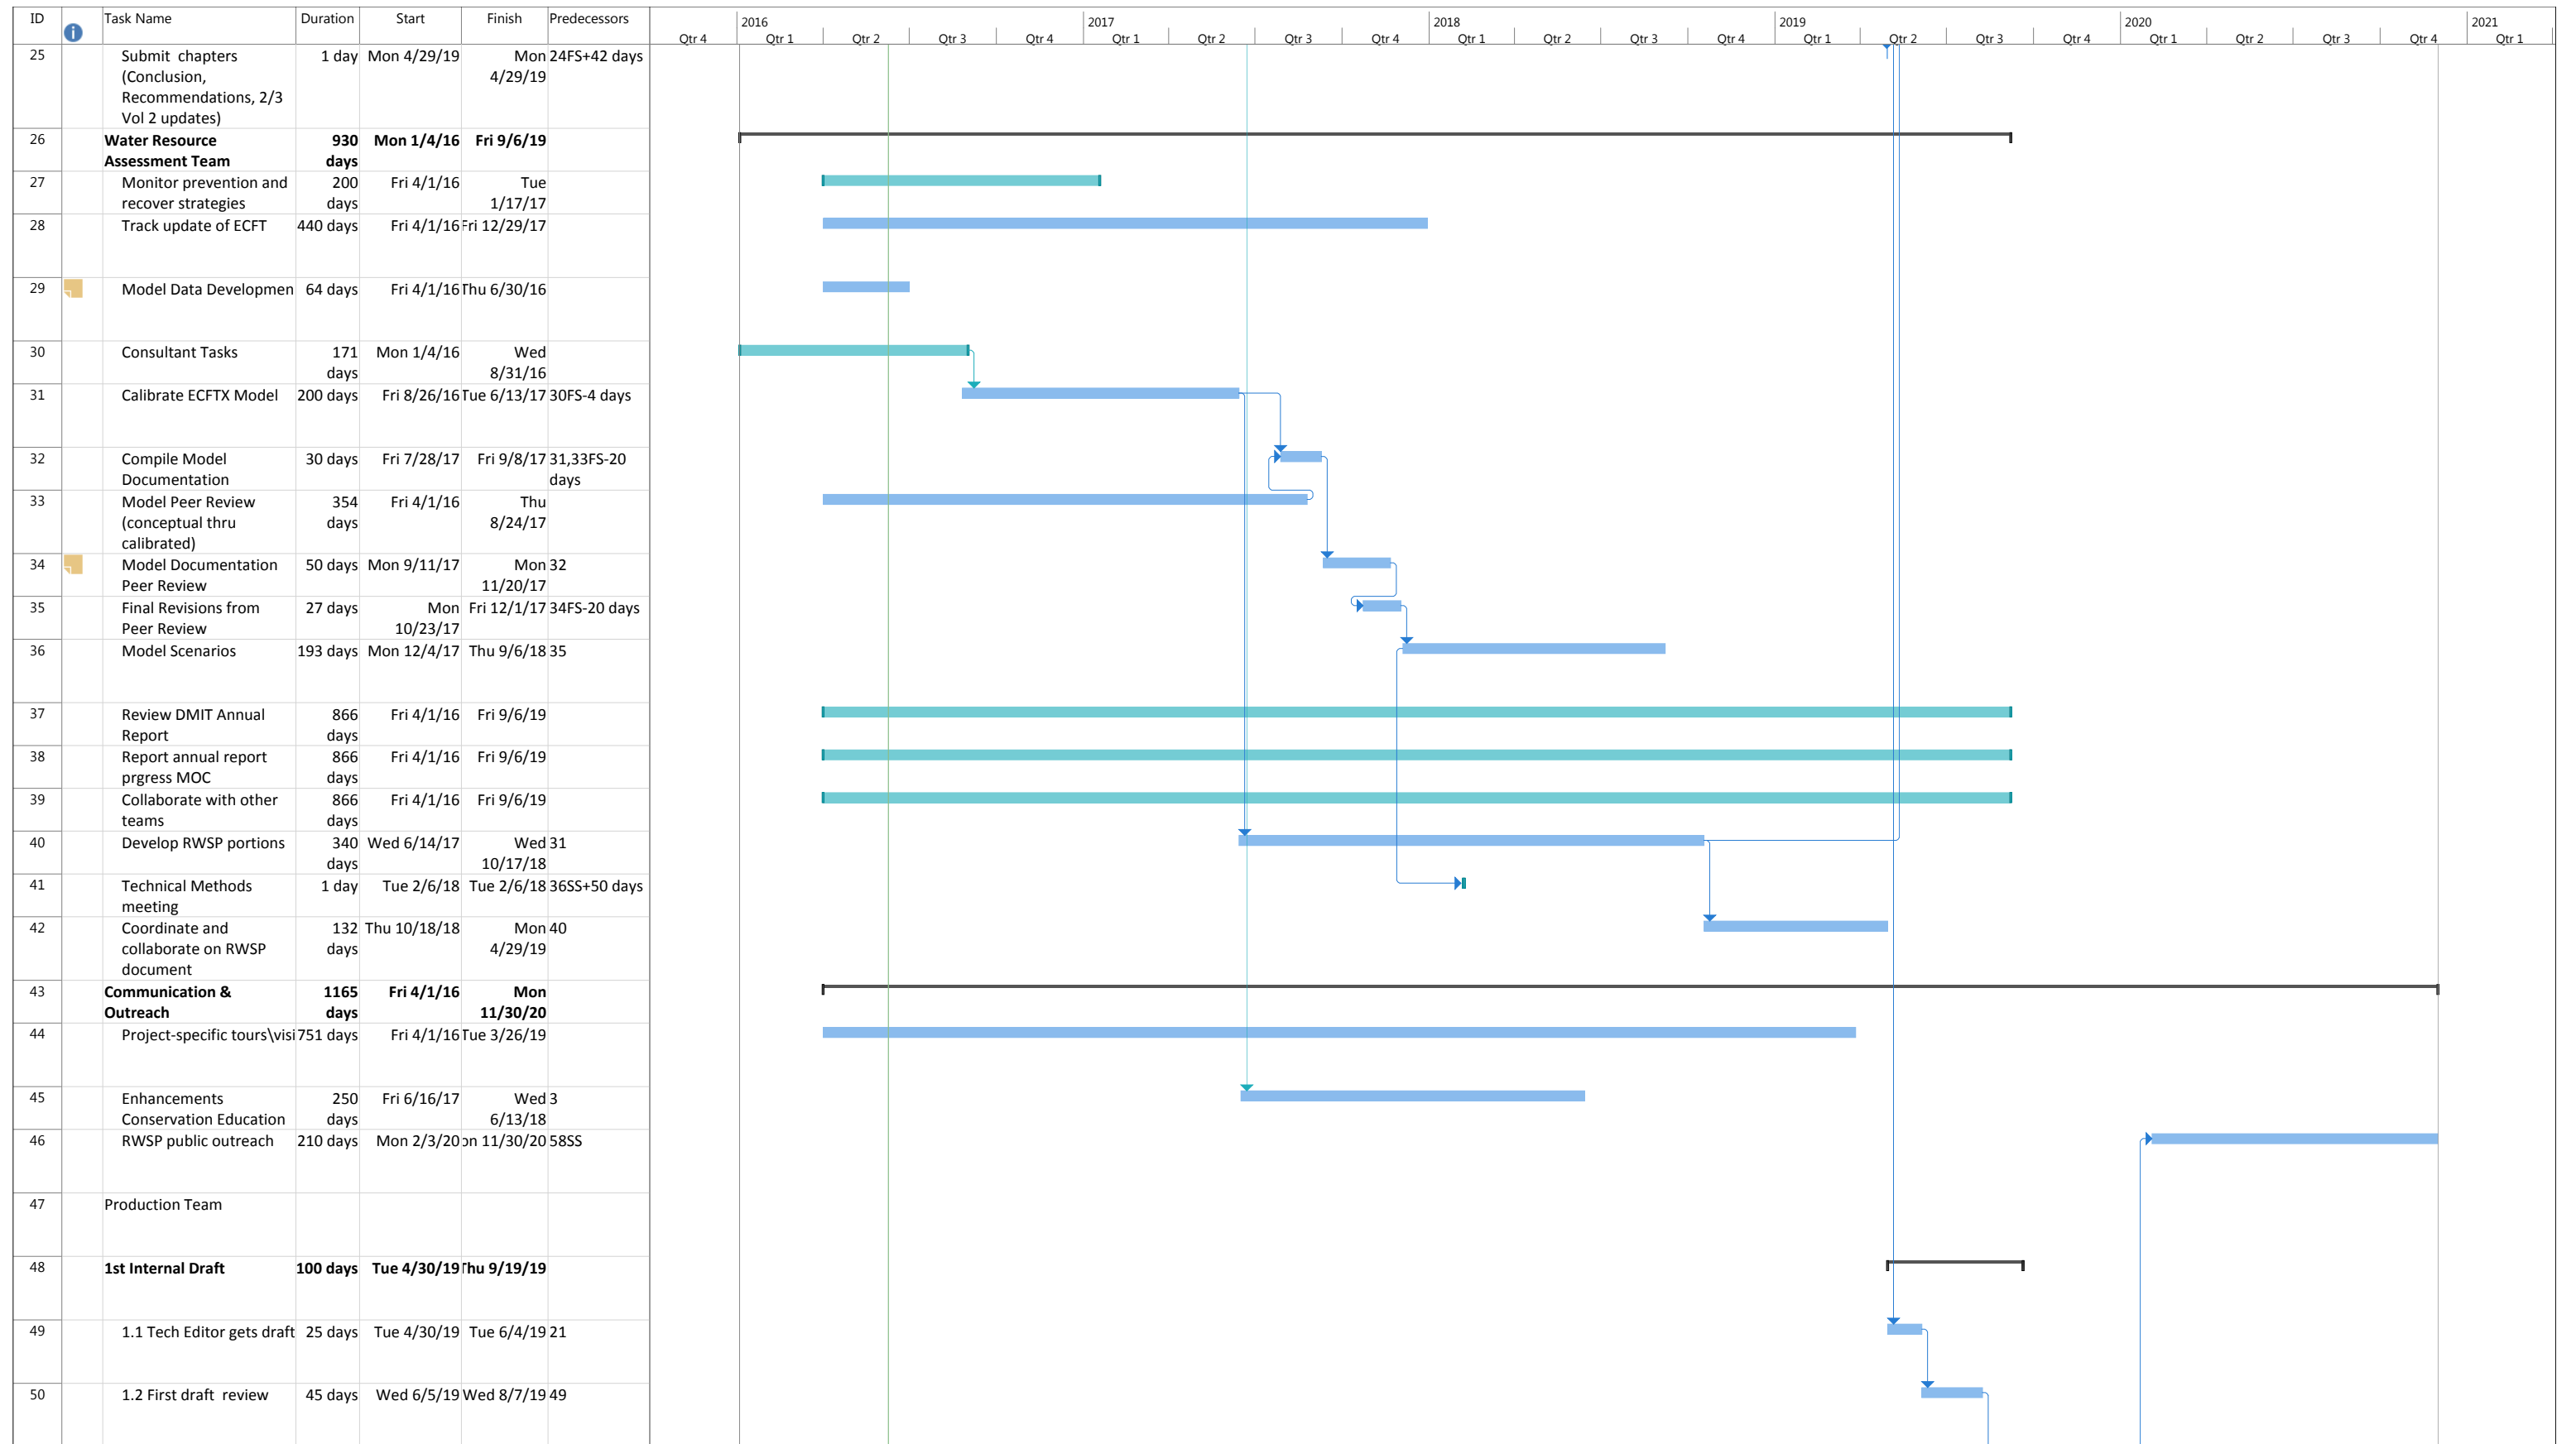

Project: CFWI MASTER 040116
Date: Thu 6/9/16



ID	Task Name	Duration	Start	Finish	Predecessors	2016				2017				2018				2019				2020				2021
						Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
51	1.3 Consolidate commen	30 days	Thu 8/8/19	Thu 9/19/19	50																					
52	2nd Internal Draft	65 days	Fri 9/20/19	Thu 1/9/20																						
53	2.1 Tech Editor gets 1st draft revisions	20 days	Fri 9/20/19	Thu 10/17/19	51																					
54	2.2 Second draft review	30 days	Fri 10/18/19	Tue 12/3/19	53																					
55	2.3 Consolidate commen	15 days	Wed 12/4/19	Thu 1/9/20	54																					
56	Draft RWSP	190 days	Fri 1/10/20	Tue 10/7/20																						
57	Tech Editor gets 2nd draft revisions	15 days	Fri 1/10/20	Fri 1/31/20	55																					
58	Draft RWSP onto District websites	2 days	Mon 2/3/20	Tue 2/4/20	57																					
59	1st Regional public meeti	1 day	Wed 3/4/20	Wed 3/4/20	58FS+20 days																					
60	2nd regional public meet	1 day	Thu 4/2/20	Thu 4/2/20	59FS+20 days																					
61	3rd regional public meeti	1 day	Fri 5/1/20	Fri 5/1/20	60FS+20 days																					
62	Public comment period	79 days	Wed 2/5/20	Tue 5/26/20	58																					
63	Comments/Response Document development	79 days	Tue 4/14/20	Tue 8/4/20	62FS-30 days																					
64	Comments/Response Document review	15 days	Wed 8/5/20	Tue 8/25/20	63																					
65	Comments/Response MOC review	15 days	Wed 8/26/20	Wed 9/16/20	64																					
66	Presentation to MOC	1 day	Thu 9/10/20	Thu 9/10/20	65FS-5 days																					
67	MOC deadline review	0 days	Wed 9/16/20	Wed 9/16/20	65																					
68	RWSP draft to Tech edito	15 days	Thu 9/17/20	Wed 10/7/20	65																					
69	FINAL Draft RWSP	14 days	Wed 10/7/20	Tue 10/27/20																						
70	Tech editor delivers Final Draft	0 days	Wed 10/7/20	Wed 10/7/20	68																					
71	Presentation to Steering Committee	1 day	Thu 10/8/20	Thu 10/8/20	70																					
72	Final Draft on websites	2 days	Thu 10/8/20	Fri 10/9/20	70																					
73	Comment/Response document on websites	0 days	Fri 10/9/20	Fri 10/9/20	72																					
74	SJRWMD Governing Board Approval	1 day	Tue 10/13/20	Tue 10/13/20																						
75	SFWMD Governing Board Approval	1 day	Thu 10/15/20	Thu 10/15/20																						
76	SWFWMD Governing Board Approval	1 day	Tue 10/27/20	Tue 10/27/20																						
77	WEB ready RWSP	19 days	Wed 10/28/20	Tue 11/24/20																						

Project: CFWI MASTER 040116
Date: Thu 6/9/16

Task	Summary	Inactive Milestone	Inactive Milestone	Duration-only	Duration-only	Start-only	Start-only	External Milestone	External Milestone	Manual Progress	Manual Progress
Split	Project Summary	Inactive Summary	Inactive Summary	Manual Summary Rollup	Manual Summary Rollup	Finish-only	Finish-only	Deadline	Deadline	Progress	Progress
Milestone	Inactive Task	Manual Task	Manual Task	Manual Summary	Manual Summary	External Tasks	External Tasks				

